

National Broadband Plan Project Status

County Kilkenny

20th March 2023

Adam Ledwith, Stakeholder Engagement and Media Manager

Latest National Project Data

The National Broadband Plan

National Overview

Premises Surveyed: 383,423
(68% of project)

Designs Complete: 371,274
(66% of project)

Build Commenced: 279,769
(50% of project)

Premises Available for
Order/Pre-Order: 138,086

Premises Connected: 34,903

Connections Pending: 4,464

Connection Rate: 28%

RSP Contracts signed: 61

Total EOI's: 93,568


Public BCP's Installed: 281

Schools BCP's Installed: 598

County Kilkenny – Project Overview

County Kilkenny Project Overview

- There are **18,919** (up 181) premises in County Kilkenny without access to high-speed broadband
- This represents **~38%** of total premises in the county
- NBP will invest **~€72m** in delivering high-speed fibre broadband
- **The NBP in County Kilkenny is 44% complete today; which represents an investment of €30m**

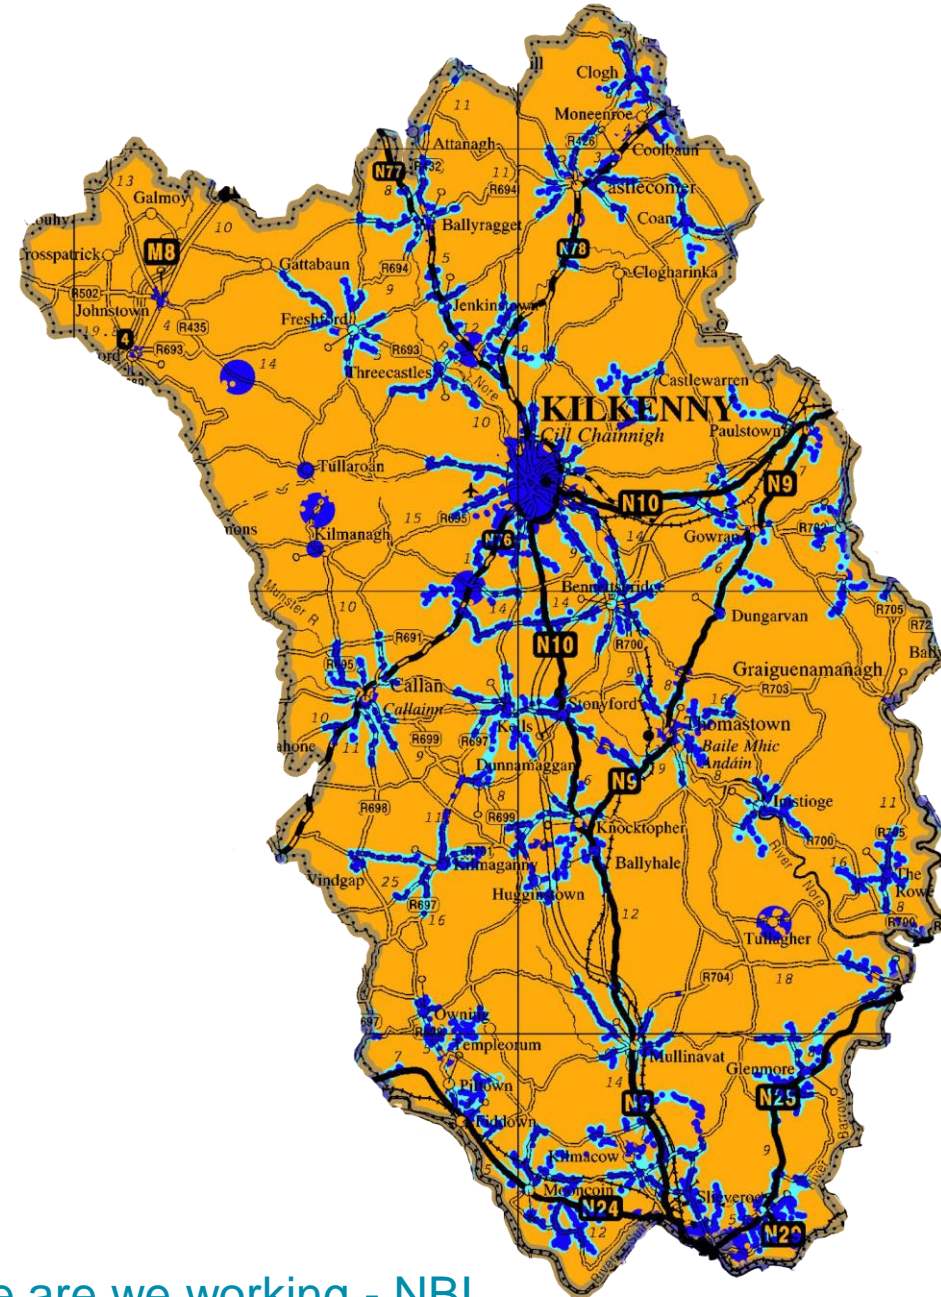

County Kilkenny – Project Data and Progress

County Kilkenny Deployment Areas – Ready for Connection now

Deployment Area	# Premises in County Kilkenny	Current Project Status	Anticipated Date For Connection
Kilkenny	3,385	Ready for Service	Available now
Waterford	2,338	Ready for Service	Available now
Johnstown	1,649	Ready for Service	Available now
Borris	862	Ready for Service	Available now
Carlow	50	Ready for Service	Available now

8,284 premises or 44% of total premises in County Kilkenny are live now for customers to place orders for connection

County Kilkenny Deployment Areas – Network Build in Progress

Deployment Area	# Premises in County Kilkenny	Current Project Status	Anticipated Date For Connection
Kilkenny	154	Network Build in Progress	March 2023 – June 2023
Johnstown	17	Network Build in Progress	March 2023 – July 2023
Waterford*	215	Network Build in Progress	August 2023 – October 2023
Borris*	165	Network Build in Progress	August 2023 – October 2023
Carrick-On-Suir*	1560	Network Build in Progress	January 2024 – June 2024
Mullinahone*	1095	Network Build in Progress	January 2024 – June 2024
Thomastown	2770	Network Build in Progress	July 2024 – December 2024

**5,976 premises (32%) are currently in the Network Build phase of the project
By end 2024 the NBP will be ~75% complete for County Kilkenny**

County Kilkenny Deployment Areas – Survey/Design stages

Deployment Area	# Premises in County Kilkenny	Current Project Status	Anticipated Date For Connection
Kilkenny	69	Survey Planned	April 2023 – June 2023
Johnstown	10	Survey Planned	April 2023 – June 2023
Castlecomer	2618	Survey Complete	July 2024 – December 2024
Ballynabola	551	Survey Underway	January 2025 – December 2026
Additional premises	131	Survey Planned	January 2025 – December 2026

County Kilkenny – Connection Data


Deployment Area	# of Premises Live	# of Active & Pending Connections
Kilkenny	3,385	952 (28%)
Johnstown	1,649	285 (23%)
Waterford	2,338	238 (22%)
Borris	862	320 (37%)
Carlow	50	10 (20%)

Kilkenny has an average connection rate of 22%. This is on par with other counties and will increase as DAs mature and awareness grows of the benefits of fibre broadband

Sign Up For Updates

The easiest way for members of the public to remain updated on the project status in their area is to **register on our website** to receive automatic updates.

www.nbi.ie/eoi



Would you like us to keep you updated?

Simply enter your eircode and email address in the boxes below to ensure you are kept up to date with the very latest information regarding the National Broadband rollout. If we have your details, we can contact you when service becomes available in your area.

<input type="text"/>	<input type="text"/>	<input type="text"/>
<input type="text"/>	<input type="button" value="KEEP UP TO DATE"/>	

NBI does not share or sell your personal information. Your data is strictly used within NBI group of companies for the purposes of the National Broadband Plan rollout. Please refer to our [Privacy Policy](#) for further information.

Additional functionality built into NBI.ie for Public Representatives

- The NBI homepage lists key stats on the project.
- Our progress is mapped and updated weekly.
- Feedback from Donegal TAG and engagement with BBOs informed our plans to build out additional functions on the website.

We are committed to connecting

560k
premises

1.1m
people

65k
farms

44k
small business

679
schools

Our progress so far

349,834
Premises surveyed

331,036
Designs complete

210,838
Premises under
construction /
constructed

88,075
Premises available
for order/pre-order


75,589
Premises Passed

18,592
Premises
Connected

708
BCPs / schools
installed by NBI



*Progress as of 02.09.22

- We have built an additional dedicated page.
- This include progress bars across all national project headings.
- We have added additional County by County data.

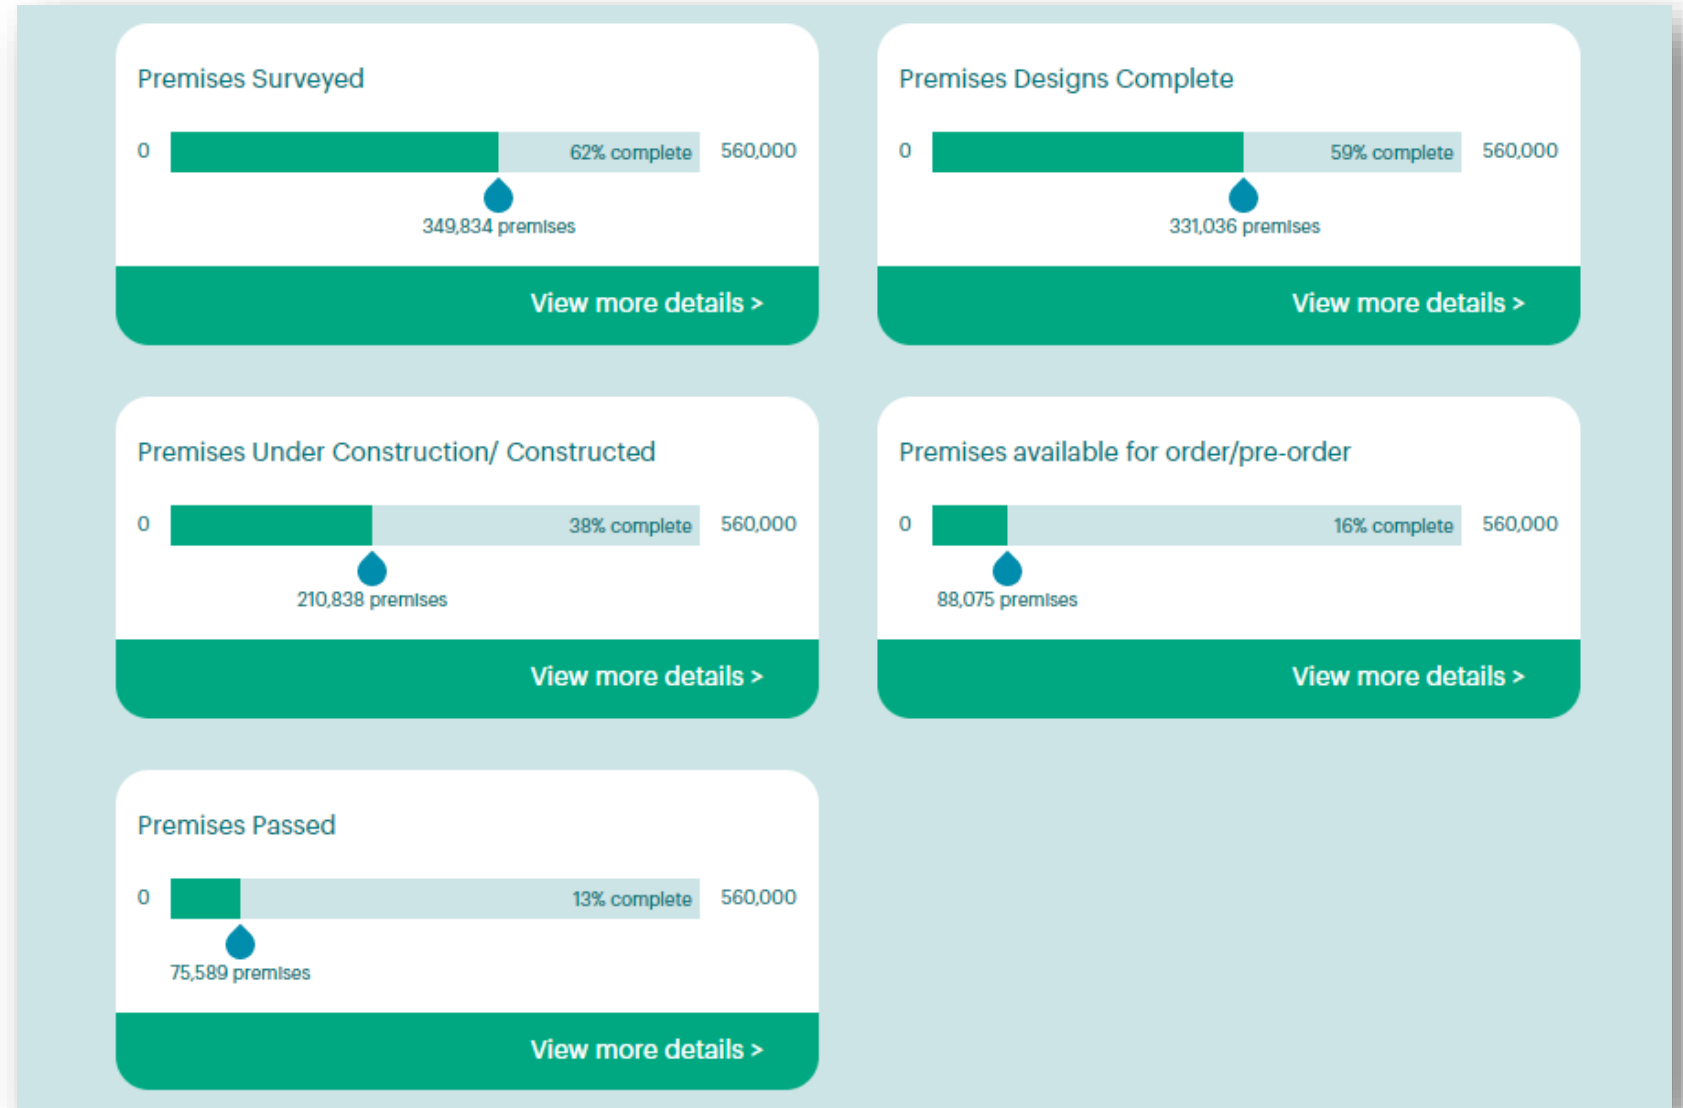

Images used here are not a live reflection of current status


- County data on website is automatically uploaded each month, sourced from the Enriched Deployment File sent to DECC.
- A new dashboard is in place to visualise the data.
- County stats, premises passed, premises connected, percentages surveyed etc.

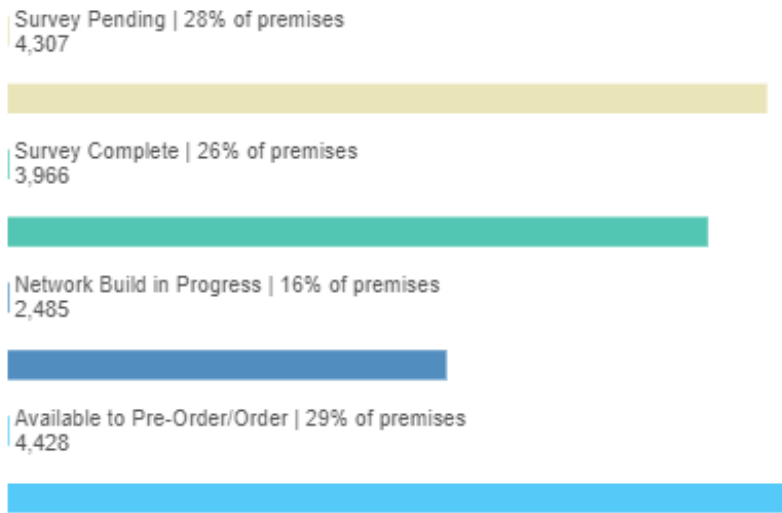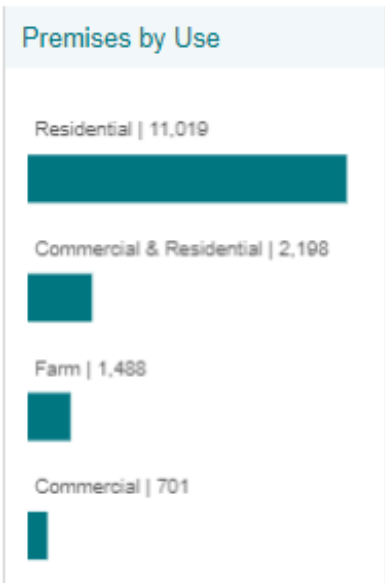

Choose your county below for more details

Waterford


Go to County Summary

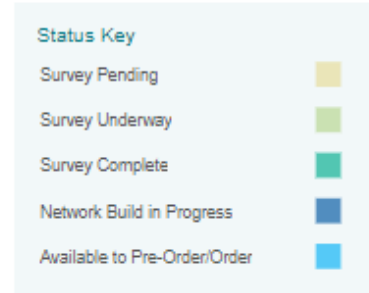

Map of Deployment Areas by Status For WATERFORD

Hover over a Deployment Area on the map for additional information.


Deployment Areas are categorised by the status key below. Please note that a Deployment Area will be marked as Available to Order/Pre-Order if 80% or more premises in the Deployment Area have services that are Available to Order/Pre-Order.

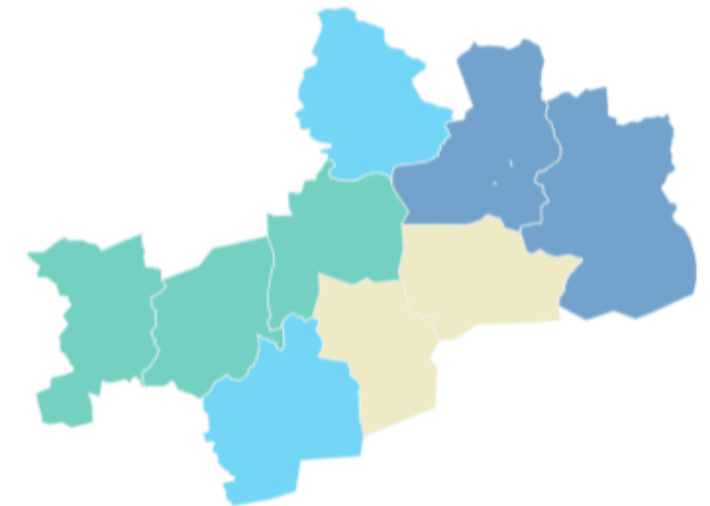

Download the latest data on your County

- County information is now in **downloadable pdf form**.
- This has been designed to be of benefit to numerous NBI stakeholders.
- We would like TDs, Councillors, BBOs and others to use this function, provide us with feedback and where possible, self-serve.
- All data headings are published.

Image used here is not a live reflection of current status




County Summary For WATERFORD

If your view is blank select a county below:

Waterford

To download a PDF version of the county summary below, click the download button to the right. In the pop up, select the page size and press 'Download'.



€59M

Investment

15K

Premises

798

Premises Passed

125

Connections

Deployment Area	Premises*	Status	Anticipated Date for Connection
BALLINAMULT	1,684	Survey Complete	January 2025 - December 2026
BONMAHON	2,115	Survey Pending	January 2025 - December 2026
CARRICK-ON-SUIR	1,380	Network Build in Progress	January 2024 - June 2024
CLONMEL	601	Available to Order/Pre-Order	Available to Pre-Order/Order
DUNGARVAN	2,068	Survey Pending	January 2025 - December 2026
FERMOY	61	Survey Complete	January 2025 - December 2026
TALLOW	2,221	Survey Complete	July 2024 - December 2024
WATERFORD	3,771	Network Build in Progress	September 2022 - October 2022
YOUGHAL	1,161	Available to Order/Pre-Order	Available to Pre-Order/Order
(Additional Premises)	344	N/A	TBC

Sign up on www.nbi.ie
to keep up to date with developments in your area

Email for political reps: reps@nbi.ie

Contact us on: **0818 624 624**
email: contactus@nbi.ie

